































































ID		Task Mod	Task Name	Duration	Remaining Duration	Start	Finish	Nov	Qtr 1, 2014 Jan
1			Space Coast TPO ITS Master Plan Scope Schedule	18 mons	160.12 da...	Feb 18 '14	Jul 17 '15		
2			Space Coast TPO ITS Master Plan	360 days	160.12 da...	Feb 18 '14	Jul 17 '15		
3			Kickoff Meeting	0 days	0 days	Feb 18 '14	Feb 18 '14		
4			Task 1 - Determine ITS Vision, Goals, & Objective	65 days	0.84 days	Feb 18 '14	May 19 '14		
5			Establish Steering Committee	15 days	0 days	Feb 18 '14	Mar 10 '14		
6			Stakeholder Meetings (Throughout Project)	1 day	1 day	Mar 11 '14	Mar 11 '14		
7			Prepare ITS Vision Statement	5 days	0 days	Mar 17 '14	Mar 21 '14		
8			Prepare ITS Goals Document	15 days	0 days	Mar 24 '14	Apr 11 '14		
9			Prepare ITS Objectives Document	15 days	0 days	Mar 24 '14	Apr 11 '14		
10			Submit Draft Documents	1 day	0 days	Apr 14 '14	Apr 14 '14		
11			Space Coast TPO Review of Draft Documents	10 days	0 days	Apr 15 '14	Apr 28 '14		
12			Prepare Final Vision, Goals, & Objectives Document	15 days	0 days	Apr 29 '14	May 19 '14		
13			Final Vision, Goals, & Objectives Document Complete	0 days	0 days	May 19 '14	May 19 '14		
14			Task 2 - Document Existing Conditions/Infrastructure	122 days	0.58 days	Apr 15 '14	Oct 6 '14		
15			Document Relevant Transportation Systems	20 days	0 days	Apr 15 '14	May 12 '14		
16			Document Communications Systems & Network	20 days	0 days	Apr 15 '14	May 12 '14		
17			Document Available FDOT Fiber	20 days	0 days	Apr 15 '14	May 12 '14		
18			Document Dissemination of Information by ISPS	20 days	0 days	Apr 15 '14	May 12 '14		
19			Document Performance Measures for Incidents	20 days	0 days	Apr 15 '14	May 12 '14		
20			Document ITS in Recent Transportation Studies	20 days	0 days	Apr 15 '14	May 12 '14		
21			Prepare Existing Conditions Document	47 days	0 days	May 30 '14	Aug 5 '14		
22			Submit Draft Existing Conditions Document	1 day	0 days	Aug 6 '14	Aug 6 '14		
23			Space Coast TPO Review of Draft Document	20 days	0 days	Aug 7 '14	Sep 4 '14		

Project: Space Coast TPO
Date: Oct 27 '14

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Critical	
Project Summary		Manual Summary		Critical Split	
Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress	

ID	Task Mod	Task Name	Duration	Remaining Duration	Start	Finish	Qtr 1, 2014	
							Nov	Jan
24	✓	Prepare Final Existing Conditions Document	21 days	0 days	Sep 5 '14	Oct 3 '14		
25		Existing Conditions Document Complete	1 day	1 day	Oct 6 '14	Oct 6 '14		
26		Task 3 - Identify Transportation ITS Needs	67 days	15 days	Aug 7 '14	Nov 10 '14		
27	✓	Assessment of County's Transportation Needs	10 days	0 days	Aug 7 '14	Aug 20 '14		
28	✓	Identify Deficiencies	3 days	0 days	Aug 21 '14	Aug 25 '14		
29	✓	Prepare Assessment/Needs Document	18 days	0 days	Aug 26 '14	Sep 19 '14		
30	✓	Submit Draft Document	1 day	0 days	Sep 22 '14	Sep 22 '14		
31	✓	Space Coast TPO Review of Draft Document	20 days	0 days	Sep 23 '14	Oct 20 '14		
32		Prepare Final Needs Document	15 days	15 days	Oct 21 '14	Nov 10 '14		
33		Transportation ITS Needs Document Complete	0 days	0 days	Nov 10 '14	Nov 10 '14		
34		Task 4 - Identification of Applicable ITS Strategies	76 days	51 days	Sep 23 '14	Jan 12 '15		
35	✓	Deficiencies Assessment	20 days	0 days	Sep 23 '14	Oct 20 '14		
36		Identify ITS Options for Resolution	10 days	5 days	Oct 21 '14	Nov 3 '14		
37		Prepare Technical Memorandum	15 days	15 days	Nov 4 '14	Nov 24 '14		
38		Submit Draft Technical Memorandum	1 day	1 day	Nov 25 '14	Nov 25 '14		
39		Space Coast TPO Review of Draft Memorandum	15 days	15 days	Nov 26 '14	Dec 18 '14		
40		Prepare Final Technical Memorandum	15 days	15 days	Dec 19 '14	Jan 12 '15		
41		Technical Memorandum Complete	0 days	0 days	Jan 12 '15	Jan 12 '15		
42		Task 5 - Regional Architecture	66 days	66 days	Nov 26 '14	Mar 4 '15		
43		Review Market Packages for National ITS Architecture	15 days	15 days	Nov 26 '14	Dec 18 '14		
44		Review ITS Options	5 days	5 days	Dec 19 '14	Dec 26 '14		
45		Develop Regional ITS Architecture	15 days	15 days	Dec 29 '14	Jan 20 '15		
46		Submit Draft Regional ITS Architecture Report	1 day	1 day	Jan 21 '15	Jan 21 '15		

Project: Space Coast TPO
Date: Oct 27 '14


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Critical	
Project Summary		Manual Summary		Critical Split	
Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress	

ID	Task Mod	Task Name	Duration	Remaining Duration	Start	Finish	Qtr 1, 2014	
							Nov	Jan
47		Space Coast TPO Review of Draft Report	15 days	15 days	Jan 22 '15	Feb 11 '15		
48		Prepare Final Regional ITS Architecture Report	15 days	15 days	Feb 12 '15	Mar 4 '15		
49		Regional ITS Architecture Report Complete	0 days	0 days	Mar 4 '15	Mar 4 '15		
50		Task 6 - Concept of Operations	51 days	51 days	Jan 22 '15	Apr 2 '15		
51		Update Existing Concept of Operations	20 days	20 days	Jan 22 '15	Feb 18 '15		
52		Submit Draft Concept of Operations	1 day	1 day	Feb 19 '15	Feb 19 '15		
53		Space Coast TPO Review of Draft ConOps	15 days	15 days	Feb 20 '15	Mar 12 '15		
54		Prepare Final Concept of Operations	15 days	15 days	Mar 13 '15	Apr 2 '15		
55		Concept of Operations Complete	0 days	0 days	Apr 2 '15	Apr 2 '15		
56		Task 7 - Prioritized ITS Master Plan	105 days	105 days	Feb 20 '15	Jul 17 '15		
57		Develop ITS Projects Deployment Plan	25 days	25 days	Feb 20 '15	Mar 26 '15		
58		ITS Projects Assessment	5 days	5 days	Mar 27 '15	Apr 2 '15		
59		Develop Implementation Plan	15 days	15 days	Apr 3 '15	Apr 23 '15		
60		Prepare Draft ITS Master Plan	24 days	24 days	Apr 24 '15	May 28 '15		
61		Submit Draft ITS Master Plan	1 day	1 day	May 29 '15	May 29 '15		
62		Space Coast TPO Review of Draft Plan	20 days	20 days	Jun 1 '15	Jun 26 '15		
63		Prepare Final ITS Master Plan	15 days	15 days	Jun 29 '15	Jul 17 '15		
64		ITS Master Plan Complete	0 days	0 days	Jul 17 '15	Jul 17 '15		
65		Scope of Services Final Completion	0 days	0 days	Jul 17 '15	Jul 17 '15		




Project: Space Coast TPO
Date: Oct 27 '14

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Critical	
Project Summary		Manual Summary		Critical Split	
Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress	

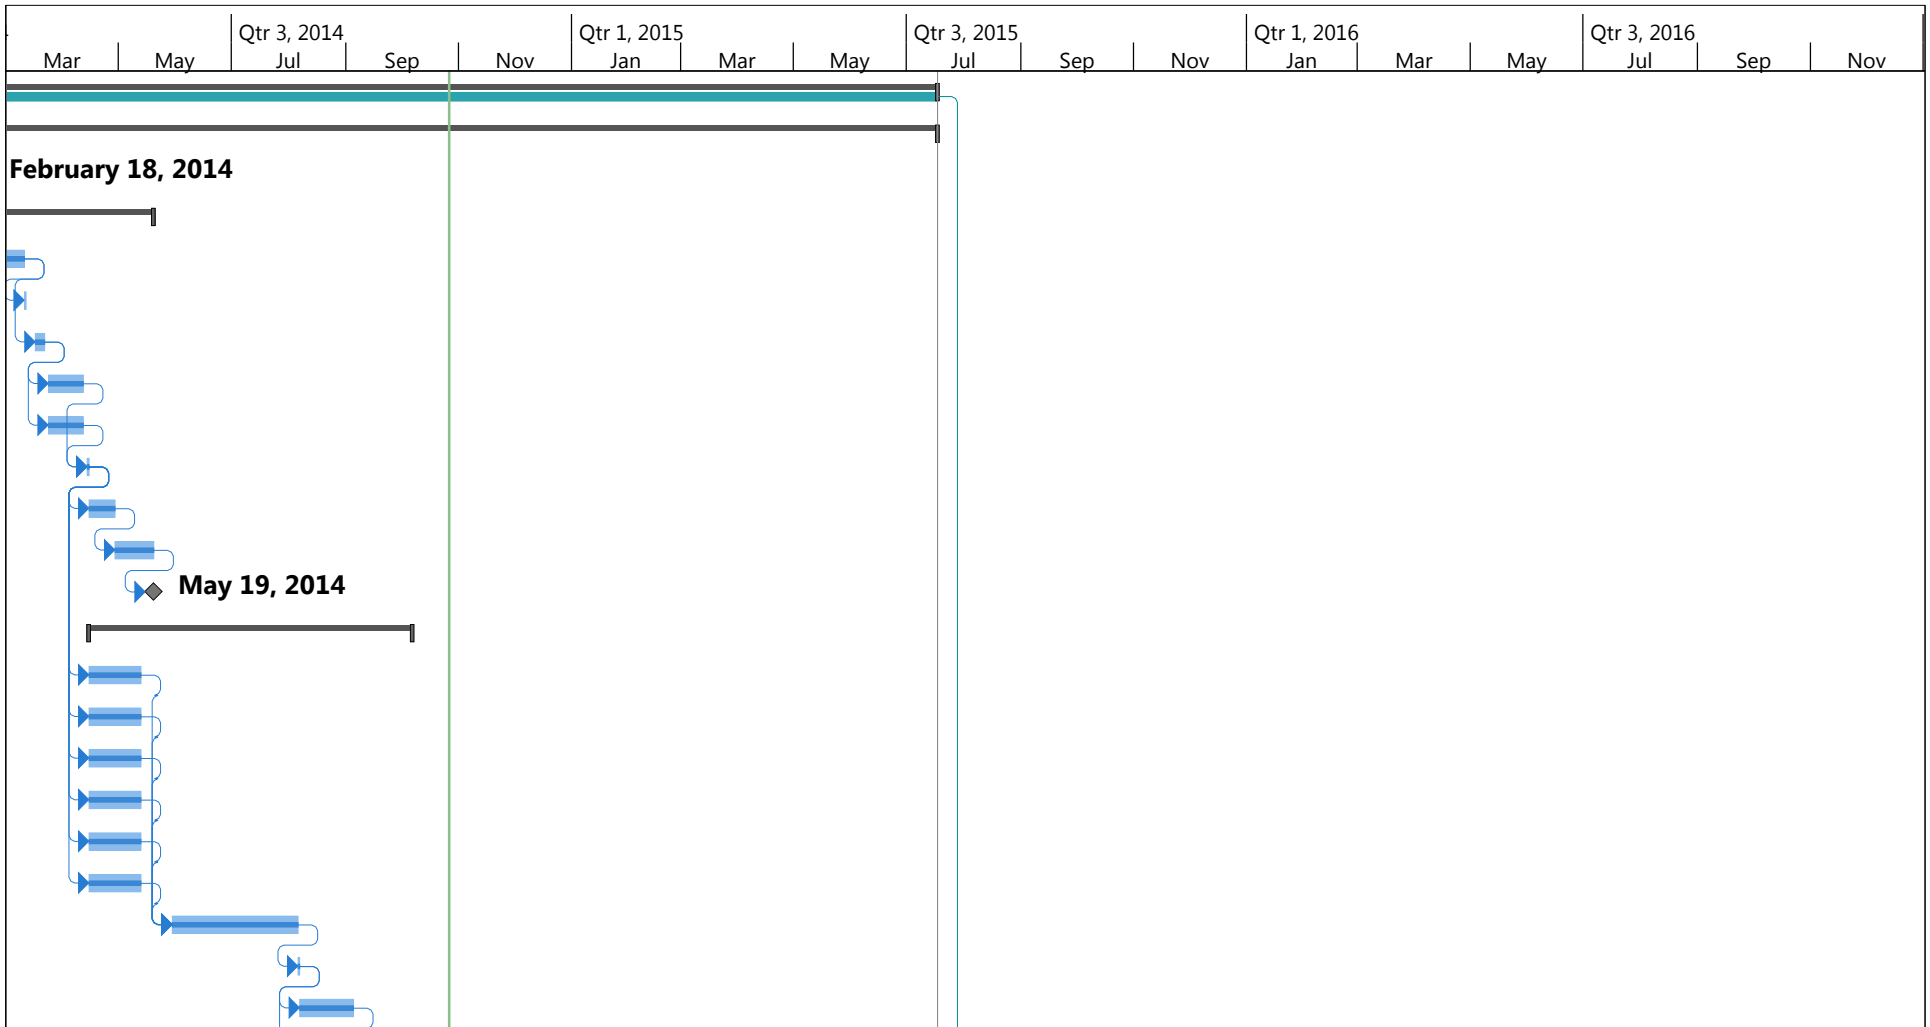


Project: Space Coast TPO
Date: Oct 27 '14

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Critical	
Project Summary		Manual Summary		Critical Split	
Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress	

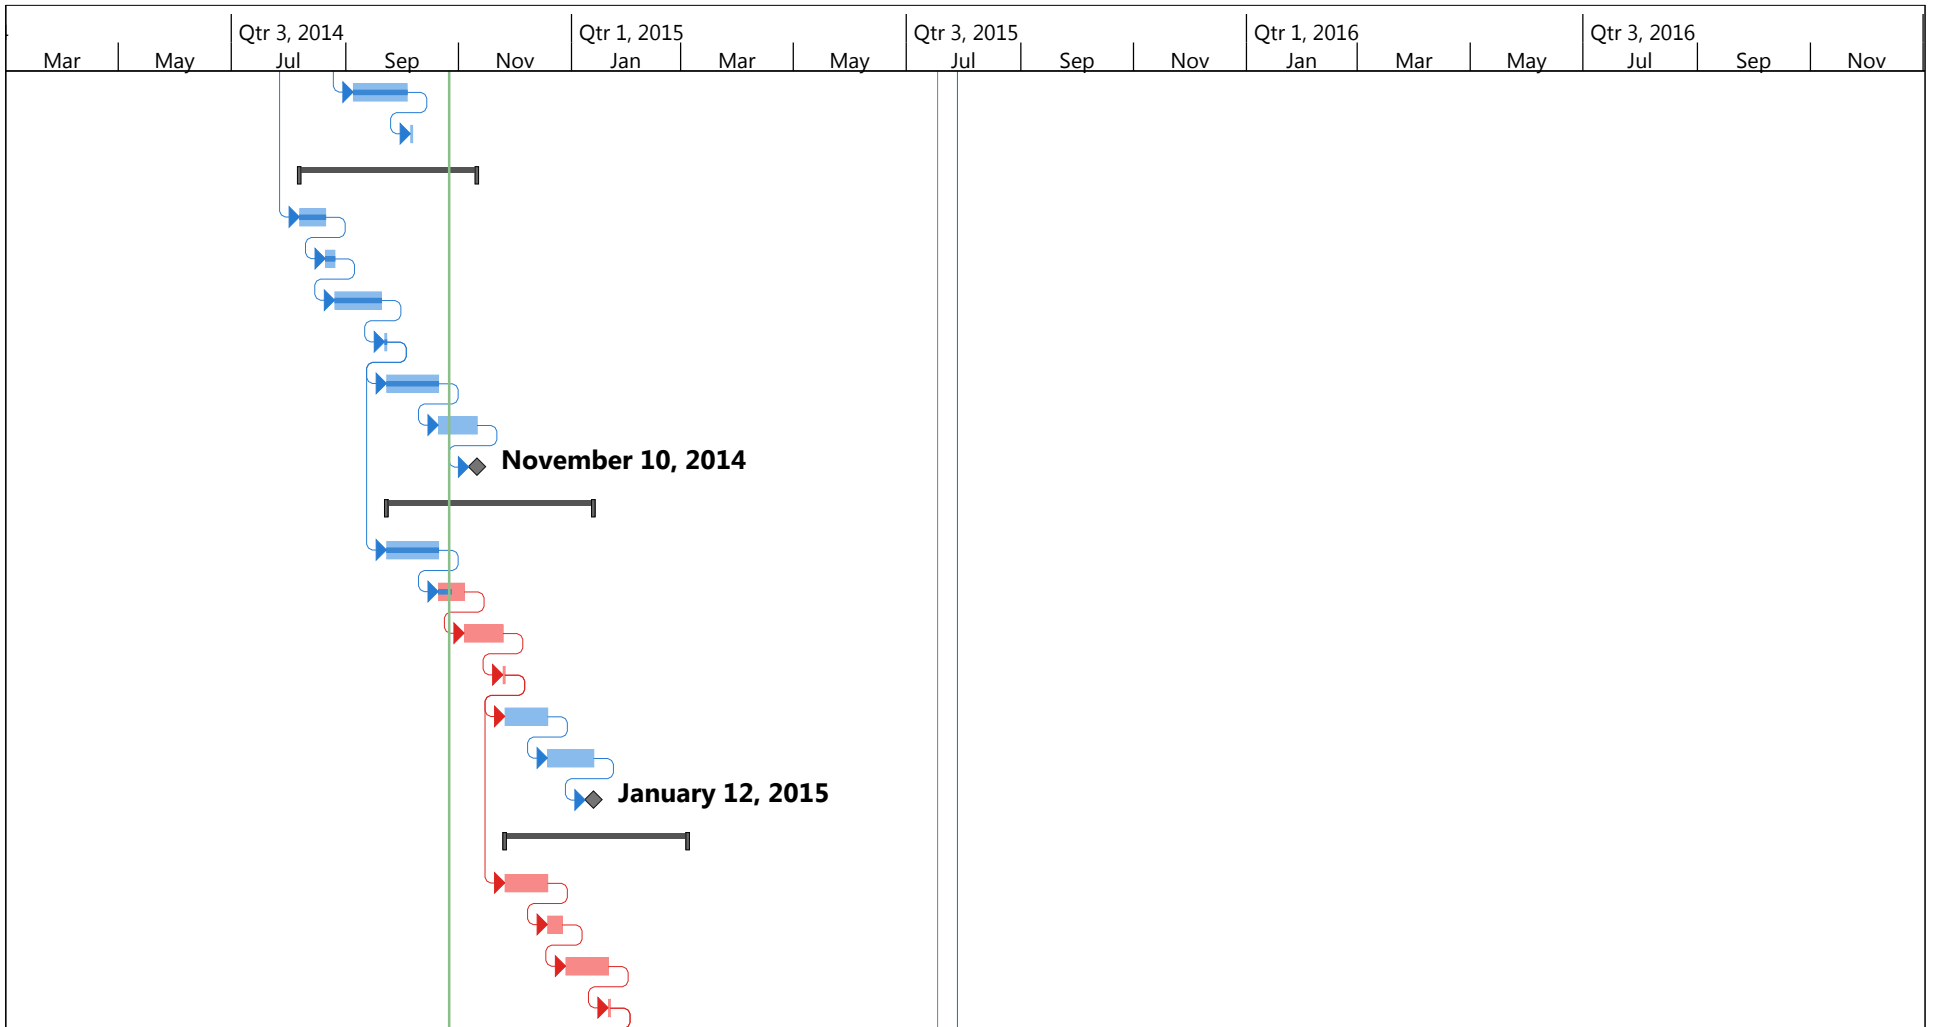

Project: Space Coast TPO
Date: Oct 27 '14

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Critical	
Project Summary		Manual Summary		Critical Split	
Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress	

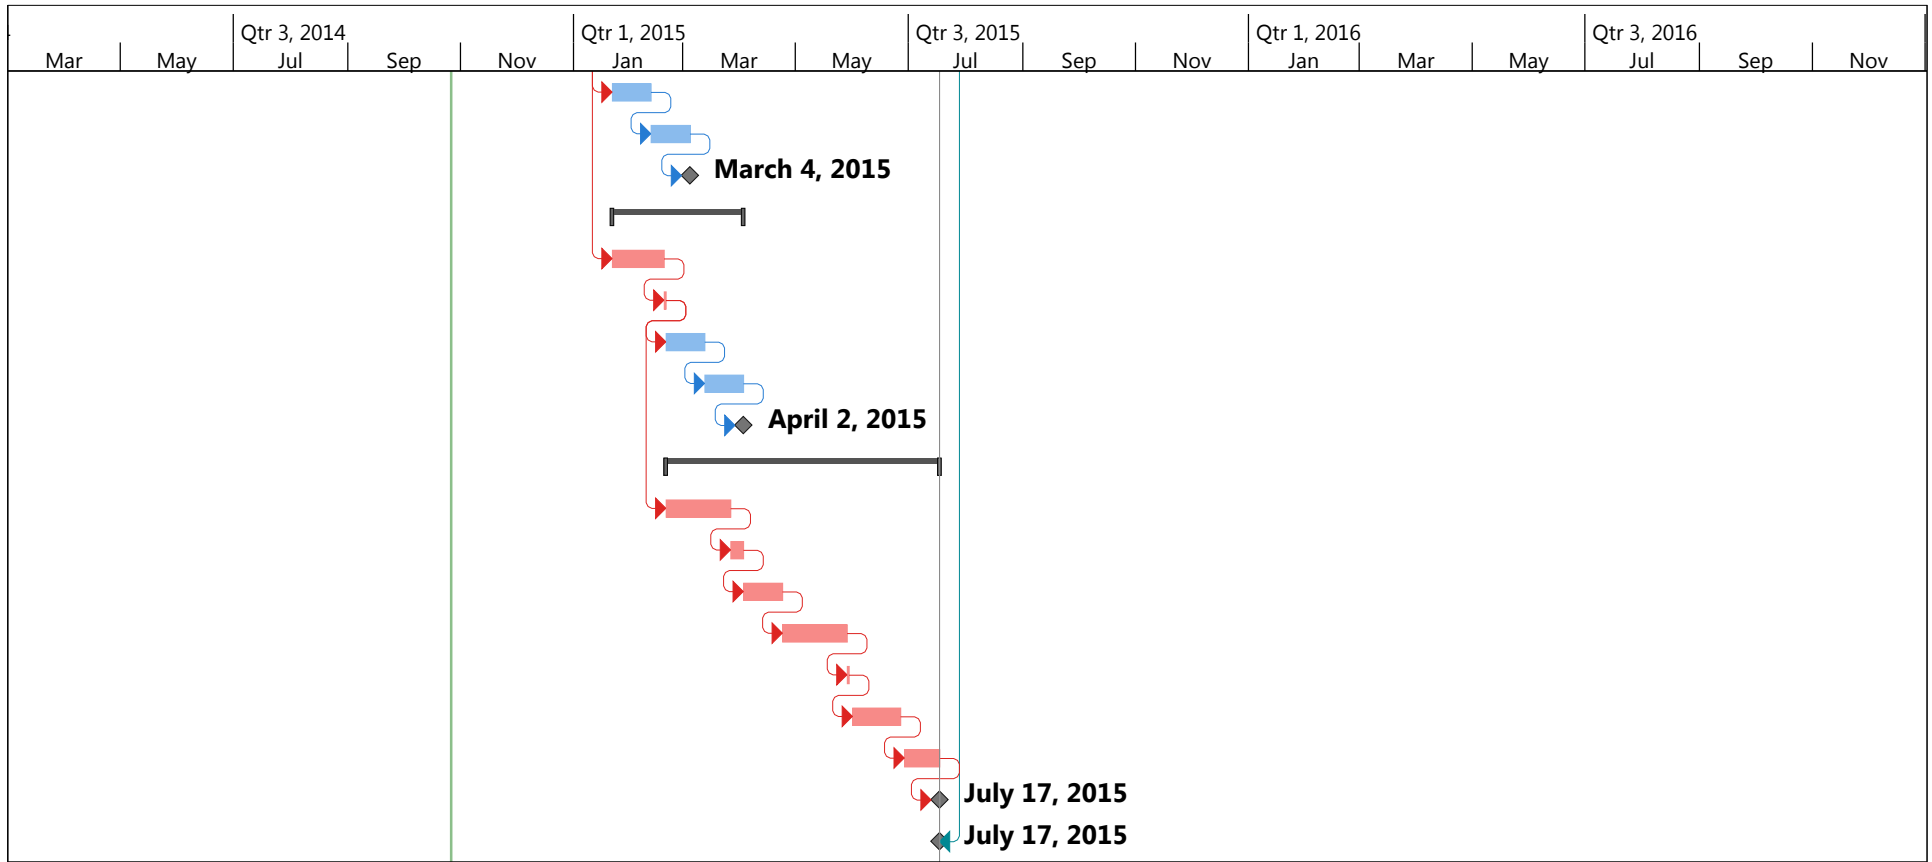

Project: Space Coast TPO Date: Oct 27 '14	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	
