

US1 PROJECTS - BREVARD COUNTY

as of 1/26/11

HIGHEST PROGRAMMED PHASE

| PHASE | COLOR |
|--------------|--------|
| P. D. & E. | Yellow |
| PREL. ENG. | Blue |
| RIGHT OF WAY | Red |
| CONSTRUCTION | Green |



**237592-2 (PTG) C8314 3.842miles
N of Pine St to N of Cidco Rd.**
 DESIGN - Complete
 (Plans update begins 2/11)
 ROW - Complete
 CST - \$26.059m FY13
 UTIL - \$ 8.000m FY13
 CEI - \$ 3.780m FY13
 LETTING = 12/5/2012

**237592-1 (PTG) C8314 0.804miles
Rosa Jones to Pine St.**
 PROJECT COMPLETED- 9/2010

**237576-2 (KCG) C8320 2.164miles
Park to Rosa Jones**
 PROJECT COMPLETED- 9/2010

**237576-3 KCG C8320 0.25miles
Barnes Blvd. West of US 1 Intersect.**
 CONTRACTOR - HALIFAX PAVING, INC.
 CONTRACT AMOUNT - \$1.499m FY10
 WORK TO BEGIN - 7/10
 EST. COMPLETION - 2/2011

NOTE:
 - Dollars are in millions
 - Dollar amounts are calculated to the year shown
 - Dollar amounts on unfunded phases are PDC.
 - Fiscal Year (FY) = July 1 to June 30

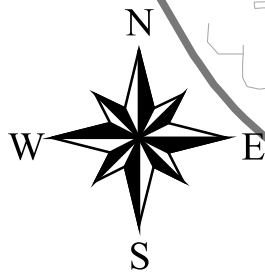

LEGEND

- US Highway
- Interstate Highway
- State Highway
- County Highway
- Railroad

